

Lab 2: Agile Backlog Creation & Sprint Simulation in Jira


Pet Adoption and Shelter Management System (PASMS)

NAME: Harsimran Kaur

SRN: PES1UG24CS187

1. Epics and Backlog Overview

The backlog was organized into four Epics, each representing a theme derived from the Lab 1 functional requirements for the Pet Adoption and Shelter Management System.

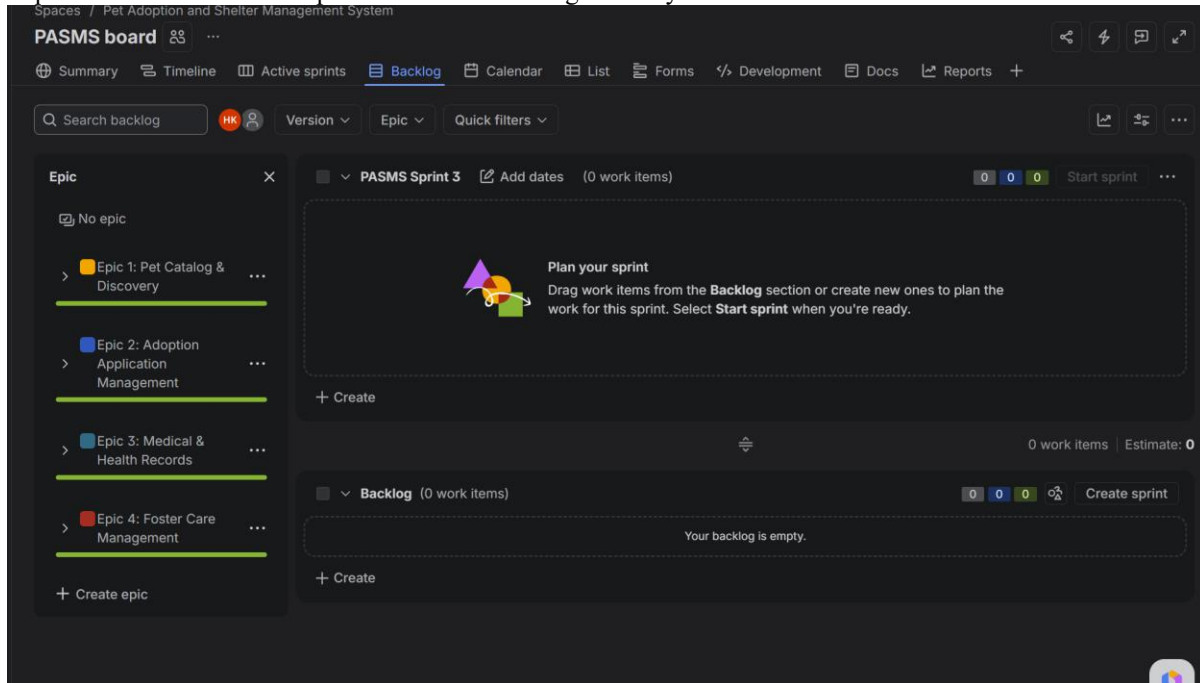

2. Epics with User Stories, Priority, and Story Points

Epic 1: Pet Catalog & Discovery

Spaces / Pet Adoption and She... / PASMS-1

Epic 1: Pet Catalog & Discovery

+ ... ⇅

> Description

Child work items 100% Done

Work	Priority	Story ...	Assig...	Status
☒ PASMS-5 Story 1.1: Search Pets	Hi...	5	Unassigned	Done
☒ PASMS-13 Story 1.2: View Pet Profile	M...	2	Unassigned	Done

Linked work items

Add linked work item

Confluence content

Project plan [Try template](#)

Agents Uses AI. Verify results.

Start work

Epic 2: Adoption Application Management

Spaces / Pet Adoption and She... / PASMS-2

Epic 2: Adoption Application Management

+ ... ⇅

> Description

Child work items 100% Done

Work	Priority	Story ...	Assig...	Status
☒ PASMS-6 Story 2.1: Submit Application	Hi...	5	Unassigned	Done
☒ PASMS-7 Story 2.2: User Authentication	Hi...	5	Unassigned	Done
☒ PASMS-8 Story 2.3: Review Application	Hi...	5	Unassigned	Done
☒ PASMS-9 Story 2.4: Approve/Reject Application	Hi...	3	Unassigned	Done
☒ PASMS-10 Story 2.5: Apply Fee Waiver	M...	2	Unassigned	Done
☒ PASMS-16 Story 2.6: Notify Applicant of Decision	M...	3	Unassigned	Done

Linked work items

Add linked work item

Confluence content

Project plan [Try template](#)

Agents Uses AI. Verify results.

To Do Agents

Improve Epic

Details

Assignee: Unassigned

Assign to me

Reporter: Harsimran Kaur

Labels: None

Due date: None

Start date: None

Priority: Medium

Development

More fields

Epic 3: Medical & Health Records

Spaces / Pet Adoption and She... / PASMS-3

Epic 3: Medical & Health Records

+ ... ≡

> Description

Child work items

100% Done

Work	Priority	Story ...	Assig...	Status
PASMS-11 Story 3.1: Log Medical Record	M...	5	Unassigned	Done
PASMS-14 Story 3.2: Update Vaccination Status	M...	3	Unassigned	Done

Linked work items

Add linked work item

Confluence content

Project plan

Try template

Agents

Start work

To Do Agents %

Improve Epic

Details

Assignee

Unassigned

Assign to me

Reporter

Harsimran Kaur

Labels

None

Due date

None

Start date

None

Priority

Medium

Development

Epic 4: Foster Care Management

Spaces / Pet Adoption and She... / PASMS-4

Epic 4: Foster Care Management

+ ... ≡

> Description

Child work items

100% Done

Work	Priority	Story ...	Assig...	Status
PASMS-12 Story 4.1: Schedule Foster Placement	M...	3	Unassigned	Done
PASMS-15 Story 4.2: Cancel Foster Placement	L...	2	Unassigned	Done

Linked work items

Add linked work item

Confluence content

Project plan

Try template

Agents

Start work

To Do Agents %

Improve Epic

Details

Assignee

Unassigned

Assign to me

Reporter

Harsimran Kaur

Labels

None

Due date

None

Start date

None

Priority


Medium

Development


More fields

3. Sprint Reports and Burndown Charts


Sprint one and sprint two were created. the core adoption story was completed in sprint one and completed all other supporting stories for all four epics in sprint two.



Sprint 1 Report

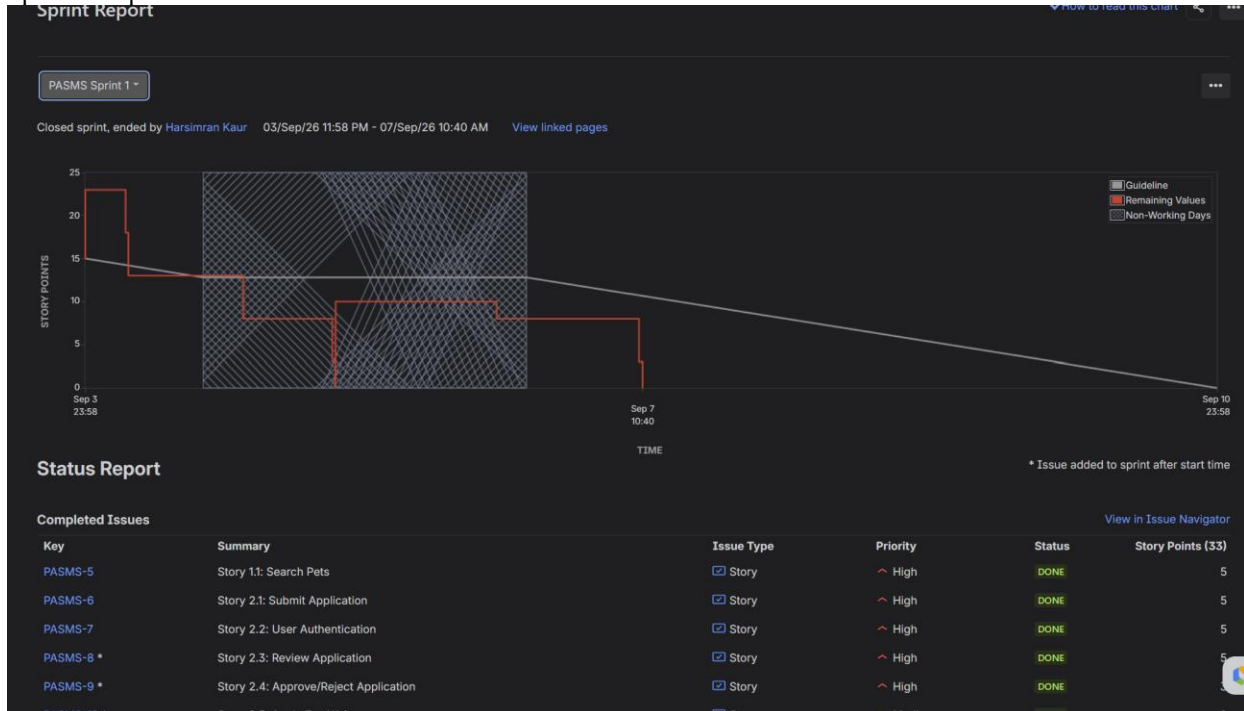

Sprint 2 Report

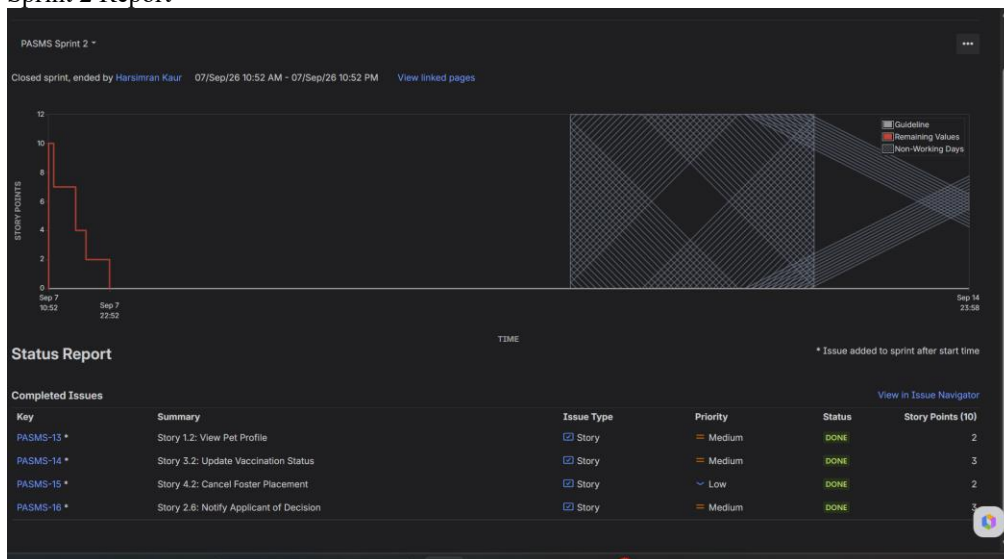

4. Reflection Questions

1. Did your estimations reflect the actual effort?

Story points were assigned using the Fibonacci scale based on the complexity of each story. Core stories like submitting an application, authenticating users, and reviewing applications were rated higher with 5 points because they involve more logic and validation, while smaller supporting stories such as applying a fee waiver or cancelling a foster placement were rated lower 2 points. Since this was a solo simulation rather than a real development effort, the points reflect relative sizing rather than measured effort, but the estimates were consistent with the actual scope of each story.

2. Was your backlog well-prioritized?

Yes. The stories that make up the adoption path, searching for a pet, submitting an application, authenticating, reviewing, and approving or rejecting, were all marked High priority, since the system cannot function without them. Supporting features such as fee waivers, medical record updates, foster placement, and applicant notifications were marked Medium or Low priority, reflecting their secondary role in the overall workflow.

3. How did your simulated sprint align with your plan?

Sprint 1 stories were completed and moved to Done across multiple days September 3 to 7. Sprint 2 followed the same approach starting from 7th September 5am to 10pm. This meant both sprints' burndown charts showed a gradual step pattern reflecting work completed over time, rather than a single instant drop.

4. What insights did the burndown chart give about your team's capacity?

The staggered burndown charts for both sprints show incremental progress over time rather than a single sharp drop, which is a more realistic representation of how work gets completed during a sprint. This shows that a burndown chart is only a useful monitoring tool when task completion is spread out naturally, marking everything Done at once will not be realistic and it will hide how work is actually progressing and would mislead a real team about their pace and capacity.
